

Parks & Recreation Department

Public Works Engineering Services


Craig Ranch Reinvestment Plan

City Council Work Session

August 5, 2009



* conceptual master plan

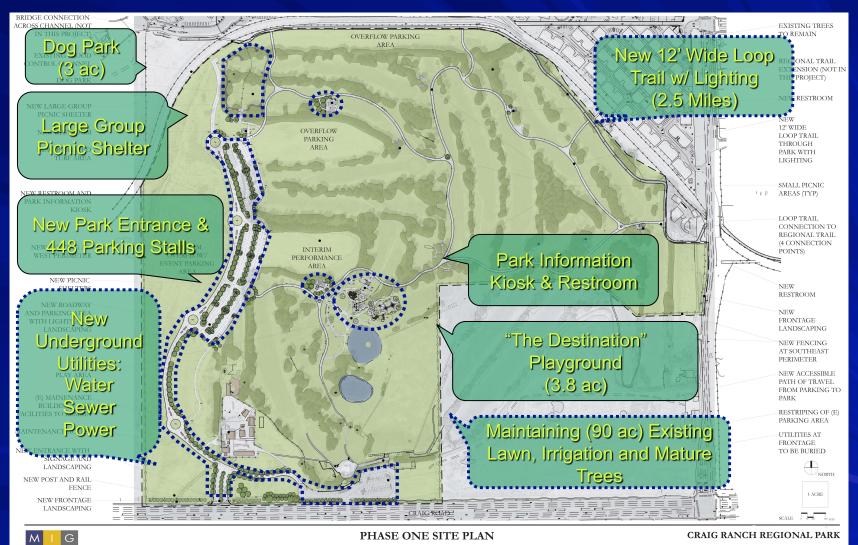


PHASE 1 – SITE LAYOUT (Start of Construction August 2009)

0

CRAIG RANCH REGIONAL PARK PHASE 2 SITE LAYOUT


Currently 40% Design, Cardno WRG INC. Includes:

- (2) Large Group Picnic Shelters
- (2) Baseball Fields
 w/ Picnic Shelter
 and Restrooms
- (6) Tennis Courts
- (4) Volleyball Courts
- (4) Basketball Courts

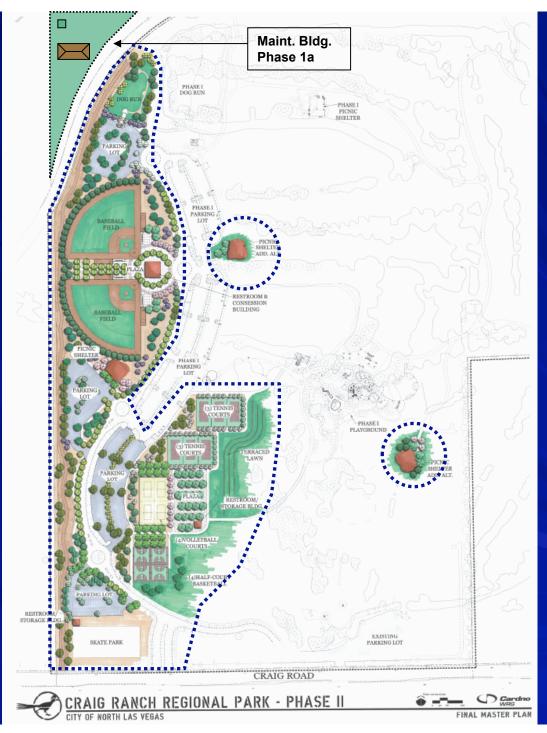

- Dog Park (2 ac)
- Skate & Bike Park
- 413 NewParkingStalls



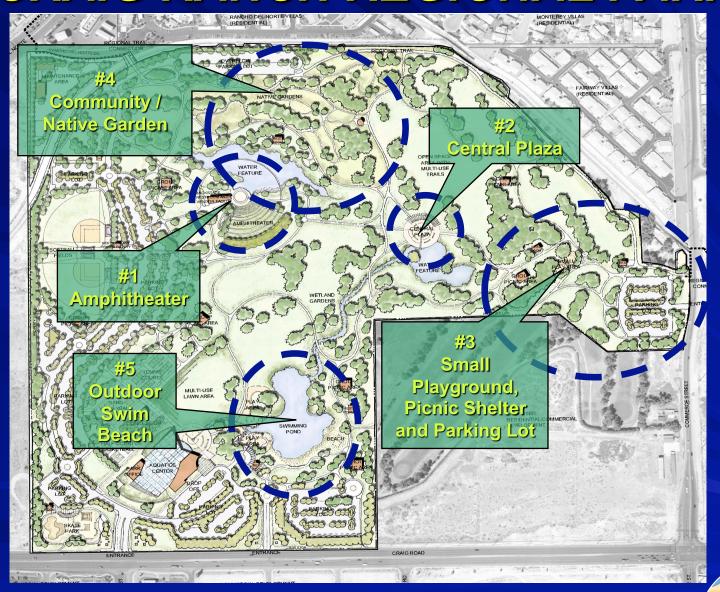

Reinvestment Strategy

- Current Bidding Climate Remains Favorable for Construction Projects
- Phase 1 Construction Budget: \$19,100,000
 (Constr. Bid = \$11.2 and a Project Savings = \$7,000,000)
- Phase 2 Construction Budget: \$19,900,000
 (Constr. Estimate = \$11.7 and a Project Savings = \$8,200,000)
- Remaining Construction Budget for the Five Park Elements: \$15,200,000
- Project Funding Source: SNPLMA Funds are Project Specific and any unspent project funds must be returned to BLM


Action:

- Direction to move forward with the Reinvestment Plan
- Establish Priority of the Five Park Elements as Referenced in the Master Plan
- Include the Five Park Elements as Bid Additive for Phase 2

Note: Staff's Recommendation Supported by PRAB, June 9, 2009

Cardno WRG Inc., Contract Amendment scheduled for August 19, 2009



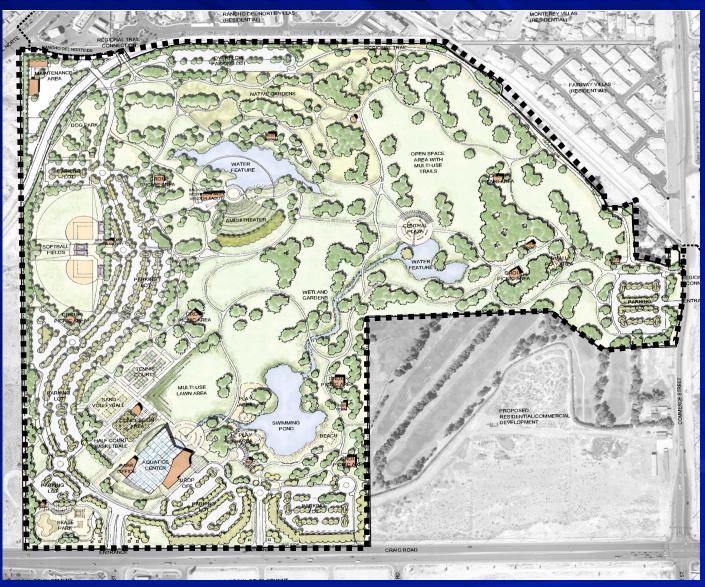

Tentative Completion: Fall 2011



Tentative Construction Schedule:

Phase 1 August 2009 - October 2010

Phase 2 Fall 2010 - Fall 2011

